Stage 1 Construction

ID	Task Name	Duration	Start	Finish
1	**Production Ponds**	**200 days**	**Mon 3/1/04**	**Fri 12/3/04**
2	Site establishment	25 days	Mon 3/1/04	Fri 4/2/04
3	Clearing and stripping	65 days	Mon 3/8/04	Fri 6/4/04
4	Earthworks	160 days	Mon 3/22/04	Fri 10/29/04
5	Structures	135 days	Mon 5/3/04	Fri 11/5/04
6	Erosion protection works	100 days	Mon 7/19/04	Fri 12/3/04
7	Relift Pump RL1	45 days	Mon 8/23/04	Fri 10/22/04
8	**Settlement Pond System**	**155 days**	**Mon 3/29/04**	**Fri 10/29/04**
9	Site clearing and stripping	15 days	Mon 3/29/04	Fri 4/16/04
10	Earthworks	40 days	Mon 4/12/04	Fri 6/4/04
11	Structures	15 days	Mon 6/7/04	Fri 6/25/04
12	Reuse pump/pipeline R1	50 days	Mon 6/28/04	Fri 9/3/04
13	Erosion protection works	60 days	Mon 8/9/04	Fri 10/29/04
14	**Admin/Processing/Workshops/Houses**	**160 days**	**Mon 3/29/04**	**Fri 11/5/04**
15	Clearing and stripping	25 days	Mon 3/29/04	Fri 4/30/04
16	Foundation earthworks	30 days	Mon 4/19/04	Fri 5/28/04
17	Offices/lab	70 days	Mon 5/31/04	Fri 9/3/04
18	Workshop	45 days	Mon 5/31/04	Fri 7/30/04
19	Machinery shed Stage 1	25 days	Mon 5/31/04	Fri 7/2/04
20	Processing/freezer	115 days	Mon 5/31/04	Fri 11/5/04
21	Feed storage shed Stage 2	35 days	Mon 5/31/04	Fri 7/16/04
22	House No. 1	90 days	Mon 5/31/04	Fri 10/1/04
23	**Potable Water Supply/Wastewater Treatment**	**135 days**	**Mon 4/26/04**	**Fri 10/29/04**
24	Upgrade freshwater dam	25 days	Mon 5/24/04	Fri 6/25/04
25	Freshwater treatment system and retic/storage	70 days	Mon 4/26/04	Fri 7/30/04
26	Processing wastewater treatment system	70 days	Mon 4/26/04	Fri 7/30/04
27	Domestic wastewater treatment/disposal system	45 days	Mon 8/30/04	Fri 10/29/04
28	**Drainage**	**41 days**	**Mon 6/7/04**	**Mon 8/2/04**
29	Main Outfall Drain	41 days	Mon 6/7/04	Mon 8/2/04
30	Drainage Relift Pump DL1	10 days	Mon 7/19/04	Fri 7/30/04
31	**Seawater Supply and Disposal System**	**155 days**	**Mon 3/1/04**	**Fri 10/1/04**
32	Disposal pump station	55 days	Mon 6/14/04	Fri 8/27/04
33	Ocean intake pipeline	60 days	Mon 4/12/04	Fri 7/2/04
34	Ocean intake screen	20 days	Mon 6/28/04	Fri 7/23/04
35	Ocean disposal pipeline	80 days	Mon 4/12/04	Fri 7/30/04
36	Intake pump station civil works	45 days	Mon 3/1/04	Fri 4/30/04
37	Intake pump station mech/elec works	45 days	Mon 4/26/04	Fri 6/25/04
38	Intake and disposal rising mains	70 days	Mon 5/17/04	Fri 8/20/04
39	Testing and commissioning	30 days	Mon 8/23/04	Fri 10/1/04
40	**Stormwater System**	**45 days**	**Mon 7/5/04**	**Fri 9/3/04**
41	Diversion floodway	7 days	Mon 7/5/04	Tue 7/13/04
42	Minor stormwater drainage works	35 days	Mon 7/19/04	Fri 9/3/04
43	**Seawater Storage**	**123 days**	**Mon 4/26/04**	**Wed 10/13/04**
44	Site establishment and clearing	25 days	Mon 4/26/04	Fri 5/28/04
45	Earthworks	75 days	Mon 5/24/04	Fri 9/3/04
46	Pump station civil works	30 days	Mon 8/23/04	Fri 10/1/04
47	Relift pump S1	23 days	Mon 9/13/04	Wed 10/13/04
48	Erosion protection	21 days	Mon 8/9/04	Mon 9/6/04
49	**Power Supply**	**200 days**	**Mon 3/1/04**	**Fri 12/3/04**
50	Upgrade supply to site	110 days	Mon 3/1/04	Fri 7/30/04
51	Reticulate power to ponds/relift pumps	68 days	Wed 9/1/04	Fri 12/3/04
52	Upgrade and extend supply to seawater intake pump station	24 days	Mon 4/26/04	Thu 5/27/04
53	Extend supply to disposal pump station	34 days	Tue 6/1/04	Fri 7/16/04
54	Emergency power supply	33 days	Mon 10/11/04	Wed 11/24/04
55	**Roads and Access**	**180 days**	**Mon 3/1/04**	**Fri 11/5/04**
56	Upgrade main access road	45 days	Mon 3/1/04	Fri 4/30/04
57	Construct internal access roads	70 days	Mon 8/2/04	Fri 11/5/04

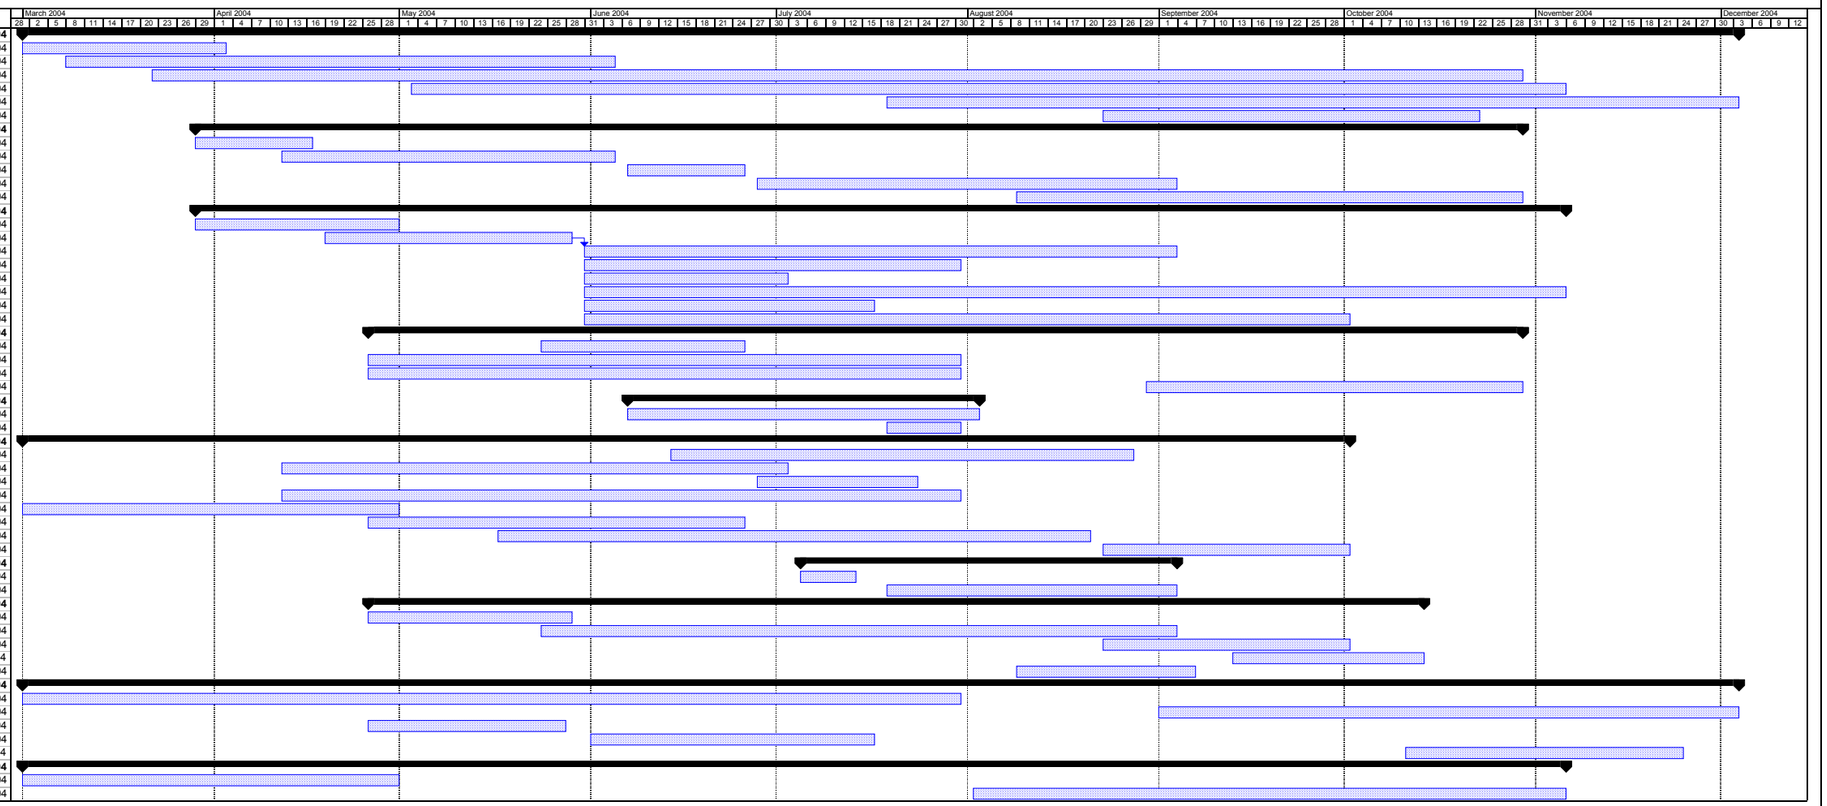

Project: Stage 1 Gannt 27_05_03
Date: Wed 5/28/03

Task | Split | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Split | Rolled Up Milestone | Rolled Up Progress | External Tasks | Project Summary | External Milestone
