Stage 3
Construction

ID	Task Name	Duration	Start	Finish
1	**Production Ponds**	**129 days**	**Wed 3/1/06**	**Mon 8/28/06**
2	Site establishment	15 days	Wed 3/1/06	Tue 3/21/06
3	Clearing and stripping	40 days	Wed 3/22/06	Tue 5/16/06
4	Earthworks	105 days	Tue 4/4/06	Mon 8/28/06
5	Structures	60 days	Wed 3/8/06	Tue 5/30/06
6	Erosion protection works	63 days	Thu 6/1/06	Mon 8/28/06
7	**Settlement Pond System**	**74 days**	**Wed 3/22/06**	**Mon 7/3/06**
8	Site clearing and stripping	21 days	Wed 3/22/06	Wed 4/19/06
9	Earthworks	68 days	Thu 3/30/06	Mon 7/3/06
10	Structures	25 days	Tue 5/30/06	Mon 7/3/06
11	Erosion protection works	40 days	Tue 5/9/06	Mon 7/3/06
12	**Power Supply**	**90 days**	**Mon 5/22/06**	**Fri 9/22/06**
13	Reticulate power to ponds	90 days	Mon 5/22/06	Fri 9/22/06
14	Emergency power supply	14 days	Tue 8/1/06	Fri 8/18/06
15	**Stormwater**	**51 days**	**Mon 5/29/06**	**Mon 8/7/06**
16	Floodway	51 days	Mon 5/29/06	Mon 8/7/06
17	**Roads and Access**	**50 days**	**Tue 7/4/06**	**Mon 9/11/06**
18	Construct internal access roads	50 days	Tue 7/4/06	Mon 9/11/06

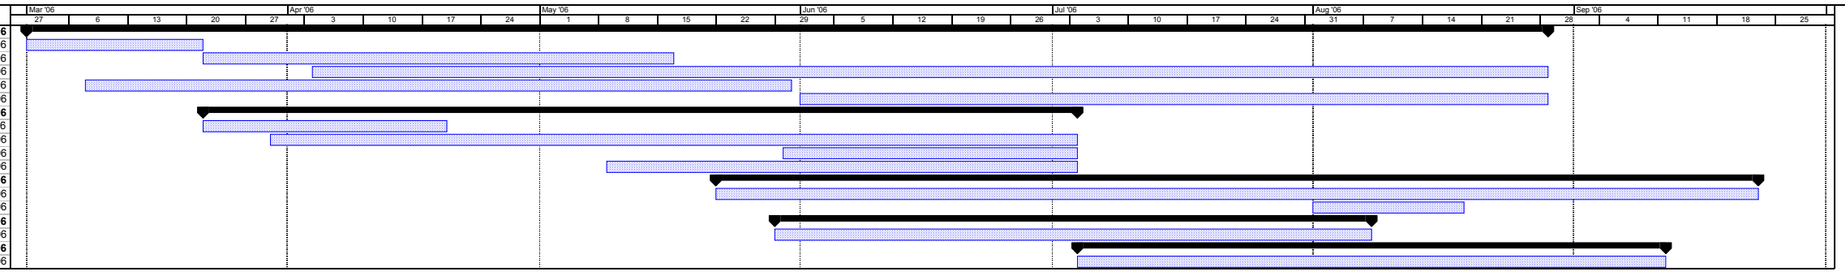

Project: Stage 3 Gannt 27_05_03
Date: Wed 5/28/03

Task | Split | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Split | Rolled Up Milestone | Rolled Up Progress | External Tasks | Project Summary | External Milestone
